Foundation Energy Management, LLC
WELLBORE DIAGRAM

Well / Battery	Prospect Name		Total Depth	Current Status
CSF 13C-11	BAXTER PASS		2186'	SI
Location	**Sec-Twn-Rng**		**Producing Horizon**	**County & State**
NWNW	11-4S-104W		MESAVERDE	RIO BLANCO, CO

WELLBORE DIAGRAM

Prepared Date: 7/24/2018
Prepared By: JARED KIMBRELL

General Info

API #: 05-103-10452

KB Elevation: 6156'
GL Elevation: 6147'

Spud Date: 8/17/2004
Completion Date: 7/24/2006

TVD: 2186
MD: XXXX'
Last PBTD: 2109 (8/20/2004)

Tubing Detail

X-X/X inch(OD)
X.X # (weight)
X-XX grade

Tubing Tally

Length	Depth
	0
	0
	0
	0
	0
	0
	0
	0
	0
	0
	0
	0
	0

Pump Details:

Pumping Unit Details:

Well Notes:

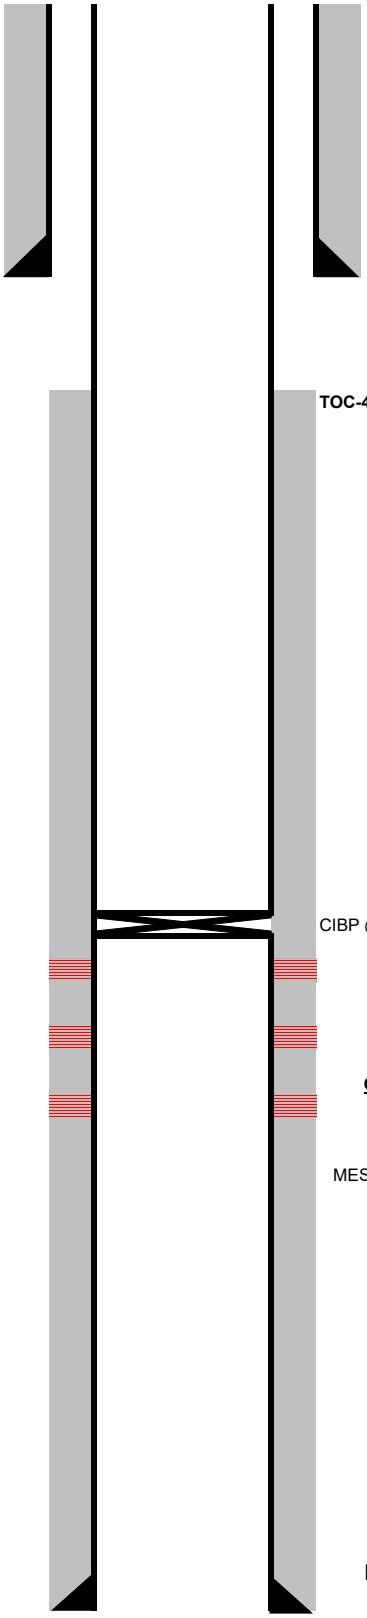

Surface Casing

8-5/8 inch (OD)
24 # (weight)
J-55 grade
260' depth from KB
0 cement top — Calculated
185 sacks of cement
12-1/4 inch (OD) HOLE SIZE

Rod Design

length	depth
	0
	0
	0
	0

Production Casing

5-1/2 inch (OD)
17 # (weight)
J-55 grade
2156' depth from KB
400' cement top — CBL
205 sacks of cement
7-7/8 inch (OD) HOLE SIZE

Open Perforations

1720'-1724' (4 SPF)
1818'-1822' (4 SPF)
1914'-1923' (4 SPF)
MESAVERDE (6/14/2006)

PBTD: 2109' (tagged on 8/20/2004)
