BISON OIL & GAS

Final - As Plugged Wellbore Schematic

Well Name:	Christiana Doll 1	Date Prepared:	1/26/2022
Location:	660 FSL & 660 FWL SWSW Sec. 30 T8N R59W	Date Surface Plug Set:	12/15/2021
County	Weld	Date Well Cut & Capped:	12/30/2021
API #:	05-123-05493		
Co-ordinates:	40.628072 / -104.027831		
Elevations:	GROUND: Unknown		
	KB: 4957'		
Depths (KB):	PBTD: --		
	TD: 6943'		

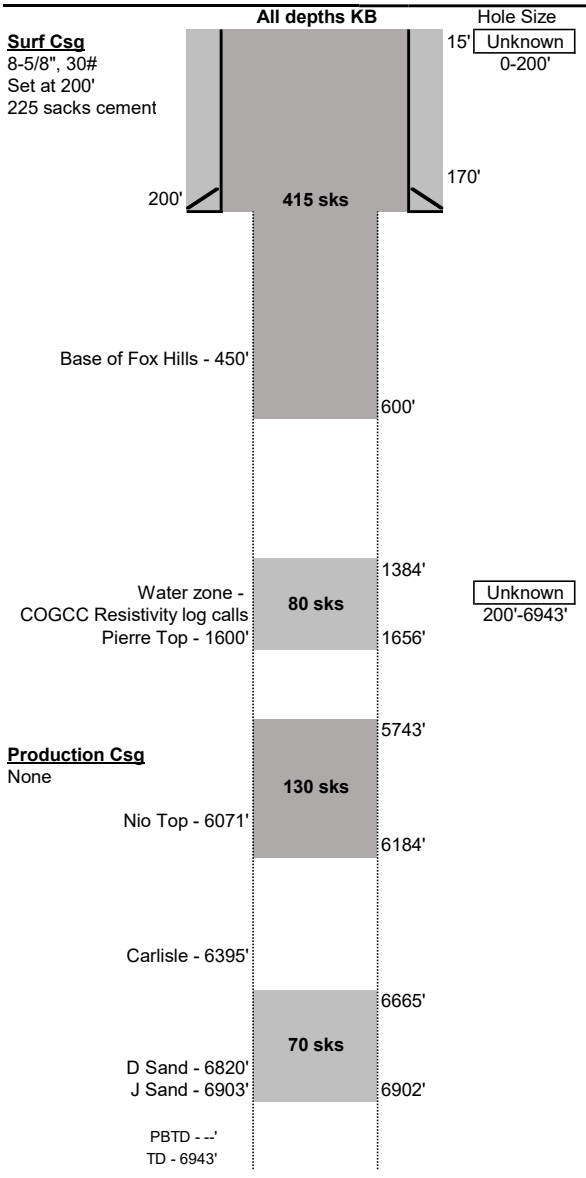

PBTD - --'
TD - 6943'

Surface Casing:
Unknown Hole Size, assumed to be 12.25"
Landed 8-5/8", 30# casing at 200'
Cemented with 225 sks

Production Casing:
No production casing

Open Hole:
200'-6943', hole size unknown, likely 7-7/8"

Tubing:
None

Rods:
None

Perforations:
None

P&A Plugs:
1. 70 sks Class G (1.15 cuft/sk) from 6665'-6902' (TOC Estimated)
2. 130 sks Class G (1.15 cuft/sk) from 5743'-6184' (TOC Estimated)
3. 80 sks Class G (1.15 cuft/sk) from 1384'-1656' (TOC Tagged)
4. 415 sks Class G (1.15 cuft/sk) from 600' to surface

Additional Notes:
Unable to reach TD and set plug at 6943', received permission from COGCC to set plug @ 6902'

Initial Potential Test:

Formation Tops:

Niobrara	6071'
Carlisle	6395'
D Sand	6820'
J Sand	6903'
