PA Wellbore For State - Vertical

Well Name: Triangle 6-22

Original Hole [Land]

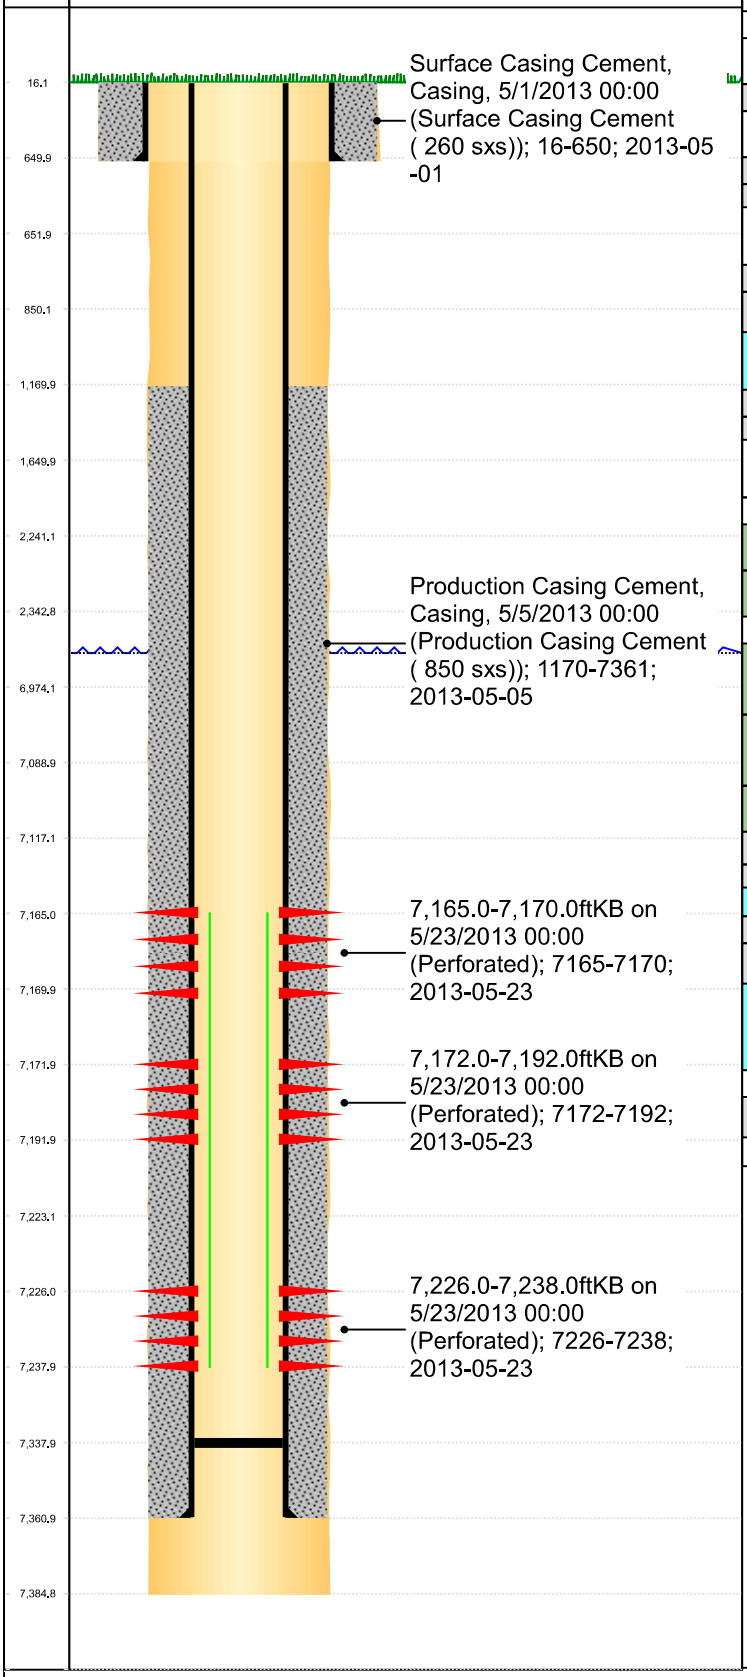

Well Header

Surface UWI	Business Unit	Gov Auth Dist	Prod Tree Loc
0512337068	Rockies	Evans	Land

Orig. KB to Gnd (ft)	Original Spud Date	Abandon Date	Well Sub-Status	High…
16.00	5/1/2013		PR	N

Comment: NO WELLFILE VALIDATED USING STATE WEBSITE

Geologic Horizons

Formation Name	Final Top MD (ftKB)

Surface Location (Congressional)

Qtr 3	Qtr 4	Section	Twnshp	Twnsh…	Range	Rng E/…	Latitude (°)	Longitude (°)
SE	NW	22	7	N	65	W	40.56192	-104.65003

Wellbore Sections

Section Des	Hole Size (in)	Top Depth (ftKB)	Btm Depth (ftKB)
Surface	12 1/2	16.0	650.0
Production	7 7/8	650.0	7,385.0

Casing Strings

Csg Des	Run Date	OD (in)	Wt/Len (lb/ft)	Grade	Top Depth (MD) (ftKB)	Set Depth (MD) (ftKB)
Surface	5/1/2013	8 5/8	24.00	J-55	16	650
Production	5/5/2013	4 1/2	11.60	N-80	16	7361

Cement

Des	Start Date	Top (ftKB)	Btm (ftKB)
Surface Casing Cement (260 sxs)	5/1/2013	16.0	650.0
Production Casing Cement (850 sxs)	5/5/2013	1,170.0	7,361.0

Stim/Frac Summary

Min Top Depth (ftKB)	Max Btm Depth (ftKB)
7,165.0	7,238.0
7,165.0	7,238.0

Perforations

Linked Zone	Date	Top Depth (ftKB)	Bottom Depth (ftKB)
NIOBRARA, Original Hole	5/23/2013 00:00	7,165.0	7,170.0
NIOBRARA, Original Hole	5/23/2013 00:00	7,172.0	7,192.0
CODELL, Original Hole	5/23/2013 00:00	7,226.0	7,238.0

Other In Hole

Run Date	Des	Make	OD (in)	Top (ftKB)	Btm (ftKB)

Logs

Date	Type	Depth Top (MD) (ftKB)	Btm (ftKB)
5/5/2012	Borehole Volume Plot	646	7,361.0
5/5/2013	Resistivity	646	7,383.0
5/23/2013	CBL/CCL/GR	0	7,320.0

Wellbore Plug Back Total Depths

Date	Type	Com	PBTD (ftKB)
11/1/2013	Fill		7,338
